



CONSTRUCTION UPDATE

Champlain Valley Educational Services Capital Project Update - Issue #25 **Monday, August 16, 2021**



Mineville's new secure vestibule construction
MINEVILLE CAMPUS

The Sprint is on!

Just like the track athletes at the Tokyo Olympics, we have entered our final sprint at the Mineville Campus and Satellite Campus. With the new school year starting in 3 weeks, our construction teams are sprinting toward the finish line. Even with the many challenges we have faced with the ongoing pandemic, construction work is on schedule at both campuses. We would like to thank our CVES 12-month staff and summer school staff for their support and flexibility while working in temporary spaces and through a wide range of construction. The construction process has been challenging, but the CVES staff has stepped up to the challenge to support the much-needed building improvements.

In this edition you will find progress photos from our Mineville Campus and our Satellite campus. Beyond the photos, at our Satellite Campus our Automatic Transfer Switch (ATS) for the generator has been shipped and is in route to the campus. This is a critical item of construction as permanent power to the building

cannot be hooked up without the ATS. Construction on the South Building will extend into September as the siding for the building is scheduled to arrive on the last day of August. This will force contractors to wait on installation of the windows and exterior doors until after the siding has arrived. Therefore, Dr. Davey and the CVES leadership team have decided to hold our opening day for staff on September 1st at the Westside Ballroom. The Instructional Services Center (ISC) lease expires at the end of September, and we are currently on schedule to have all staff at ISC move to the new campus before the end of the lease.

In school construction the end of August is a challenging, high stress, fast moving time. CVES and our contractors are working collaboratively to complete needed construction items before the end of the summer recess. As summer school has ended this past Friday on all campuses, construction expands, and the focus on the finish line remains sharp.

ANNOUNCEMENTS

The North Building, at our Satellite Campus, roofing material was scheduled to arrive in August but there has been a delay in delivery. Installation of the new roof will happen as soon as materials arrive, which is now slated for September.



MINEVILLE CAMPUS



Demolition & renovation of Mineville's Main Office area
JULY 2021



JULY-AUGUST 2021



AUGUST 2021



JULY 2021



AUGUST 2021



AUGUST 2021



JULY 2021



AUGUST 2021



Exterior work on new secure vestibule
JULY 2021



AUGUST 2021



AUGUST 2021



AUGUST 2021



AUGUST 2021



AUGUST 2021



AUGUST 2021








SATELLITE CAMPUS



AUGUST 2021



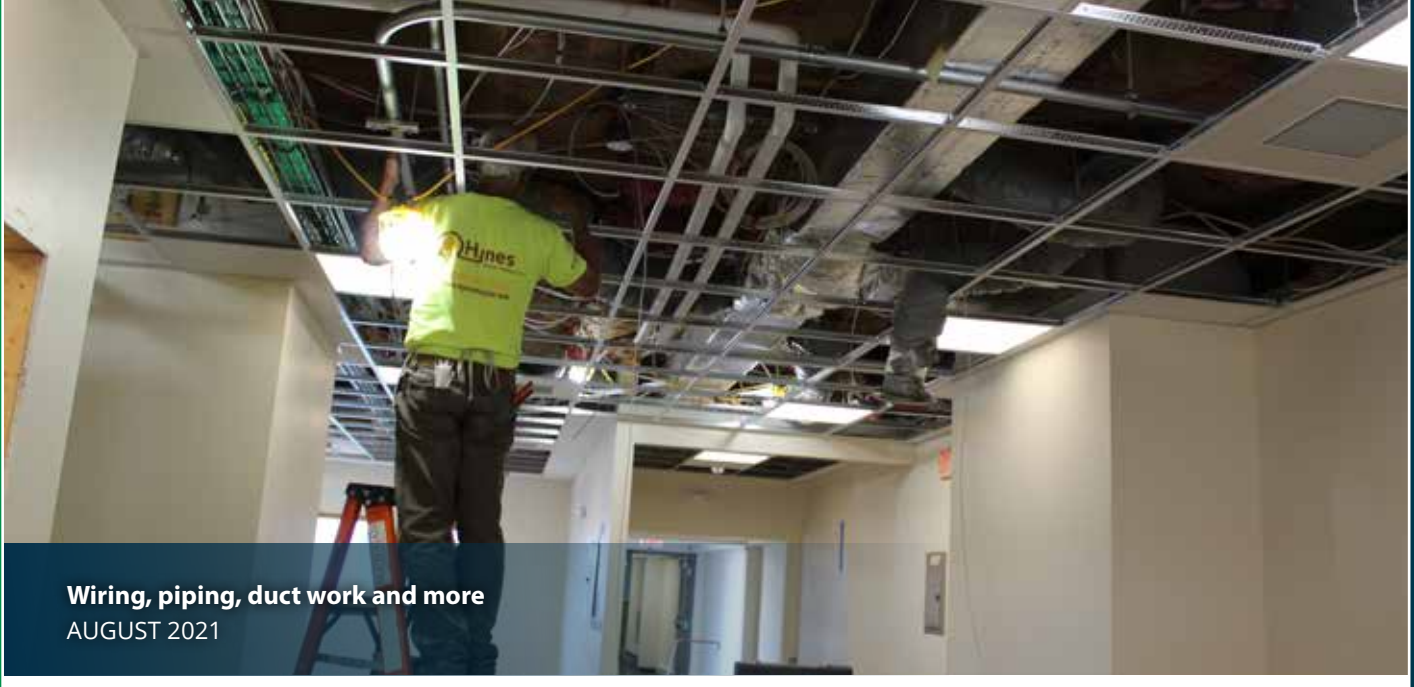

Wiring, piping, duct work and more
AUGUST 2021



FOLLOW US FOR ADDITIONAL UPDATES:



fb.me/cvesboces



twitter.com/cvesboces



www.cves.org/capitalproject
